


ID	Task Name	Duration	Start	Finish	'08 Jun 01							'08 Jun 08							'08 Jun 15								
					S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F		
1	Contracts	0 days	Sun 08/06/01	Sun 08/06/01	◆																						
2	Supply Lot Sale Agreement	0 days	Sun 08/06/01	Sun 08/06/01	◆																						
3	Supply Construction Agreement	0 days	Sun 08/06/01	Sun 08/06/01	◆																						
4	Supply Contract Plans	0 days	Sun 08/06/01	Sun 08/06/01	◆																						
5	Supply Contract Specifications	0 days	Sun 08/06/01	Sun 08/06/01	◆																						
6	Supply Contract Site Plan	0 days	Sun 08/06/01	Sun 08/06/01	◆																						
7	Secure Financing	0 days	Sun 08/06/01	Sun 08/06/01	◆																						
8	Construction Loan Settlement	0 days	Sun 08/06/01	Sun 08/06/01	◆																						
9	Document Review & Revision	25 days	Mon 08/06/02	Fri 08/07/04																							
10	Review & Finalize Plans	15 days	Mon 08/06/02	Fri 08/06/20																							
11	Review & Finalize Specifications	20 days	Mon 08/06/02	Fri 08/06/27																							
12	Review & Finalize Site Plan	1 day	Mon 08/06/23	Mon 08/06/23																							
13	Print Construction Drawings	5 days	Mon 08/06/30	Fri 08/07/04																							
14	Approve Revised Plans	0 days	Fri 08/07/04	Fri 08/07/04																							
15	Approve Revised Specifications	0 days	Fri 08/07/04	Fri 08/07/04																							
16	Approve Revised Site Plan	0 days	Fri 08/07/04	Fri 08/07/04																							
17	Bids & Contracts	24 days	Mon 08/07/07	Thu 08/08/07																							
18	Make Copies of Plans	3 days	Mon 08/07/07	Wed 08/07/09																							
19	Make Copies of Specifications	2 days	Mon 08/07/07	Tue 08/07/08																							
20	Distribute Plans & Specifications	1 day	Thu 08/07/10	Thu 08/07/10																							
21	Receive Bids	10 days	Fri 08/07/11	Thu 08/07/24																							
22	Review Bids	5 days	Fri 08/07/25	Thu 08/07/31																							
23	Sales	5 days	Fri 08/07/25	Thu 08/07/31																							
24	Construction	5 days	Fri 08/07/25	Thu 08/07/31																							
25	Execute Subcontractor Agreements	5 days	Fri 08/08/01	Thu 08/08/07																							
26	Grading & Building Permits	17 days	Mon 08/07/07	Tue 08/07/29																							
27	Schedule lot stake-out	1 day	Mon 08/07/07	Mon 08/07/07																							
28	Stake lot	1 day	Fri 08/07/11	Fri 08/07/11																							
29	File Grading Permit Application	1 day	Mon 08/07/07	Mon 08/07/07																							
30	File Building Permit Application	3 days	Mon 08/07/07	Wed 08/07/09																							
31	Post Lot Identification	1 day	Mon 08/07/14	Mon 08/07/14																							
32	Meet Sediment Control Inspector	1 day	Tue 08/07/15	Tue 08/07/15																							
33	Walk Lot w/ Owner	1 day	Wed 08/07/16	Wed 08/07/16																							

Project: b4ubuild_sample_07a
Date: Tue 16/07/12

Task		External Milestone	◆	Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone	◆	Inactive Milestone	◆	Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	↓


ID	Task Name	Duration	Start	Finish	'08 Jun 01							'08 Jun 08							'08 Jun 15						
					S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F
34	Install Construction Entrance	1 day	Thu 08/07/17	Thu 08/07/17																					
35	Install Sediment Controls	2 days	Thu 08/07/17	Fri 08/07/18																					
36	Sediment Control Insp.	1 day	Mon 08/07/21	Mon 08/07/21																					
37	Grading Permit Issued	1 day	Tue 08/07/22	Tue 08/07/22																					
38	County Permit Process	10 days	Thu 08/07/10	Wed 08/07/23																					
39	Building Permit Approved	1 day	Thu 08/07/24	Thu 08/07/24																					
40	Pay Permit Fees and Excise Taxes	1 day	Tue 08/07/29	Tue 08/07/29																					
41	Building Permit Issued	0 days	Tue 08/07/29	Tue 08/07/29																					
42	Site Work	7 days	Wed 08/07/23	Thu 08/07/31																					
43	Clear Lot	3 days	Wed 08/07/23	Fri 08/07/25																					
44	Strip Topsoil & Stockpile	1 day	Mon 08/07/28	Mon 08/07/28																					
45	Stake Lot for Excavation	1 day	Mon 08/07/28	Mon 08/07/28																					
46	Rough grade lot	1 day	Tue 08/07/29	Tue 08/07/29																					
47	Excavate for foundation	2 days	Wed 08/07/30	Thu 08/07/31																					
48	Foundation	24 days	Fri 08/08/01	Wed 08/09/03																					
49	Layout footings	1 day	Fri 08/08/01	Fri 08/08/01																					
50	Dig Footings & Install Reinforcing	1 day	Mon 08/08/04	Mon 08/08/04																					
51	Footing Inspection	0 days	Mon 08/08/04	Mon 08/08/04																					
52	Pour footings	1 day	Tue 08/08/05	Tue 08/08/05																					
53	Pin Footings	1 day	Wed 08/08/06	Wed 08/08/06																					
54	Stock Block, Mortar, Sand	1 day	Thu 08/08/07	Thu 08/08/07																					
55	Build Block Foundation	15 days	Fri 08/08/08	Thu 08/08/28																					
56	Foundation Certification	0 days	Thu 08/08/28	Thu 08/08/28																					
57	Draw #1 (Location Survey)	0 days	Thu 08/08/28	Thu 08/08/28																					
58	Fill Block Cores w/ Concrete	1 day	Fri 08/08/29	Fri 08/08/29																					
59	Steel Delivery	1 day	Mon 08/09/01	Mon 08/09/01																					
60	Set Lintels, Bolts, Cap Block	2 days	Tue 08/09/02	Wed 08/09/03																					
61	Lumber Delivery	1 day	Mon 08/09/01	Mon 08/09/01																					
62	Waterproofing and Drain Tile	1 day	Tue 08/09/02	Tue 08/09/02																					

Project: b4ubuild_sample_07a Date: Tue 16/07/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	

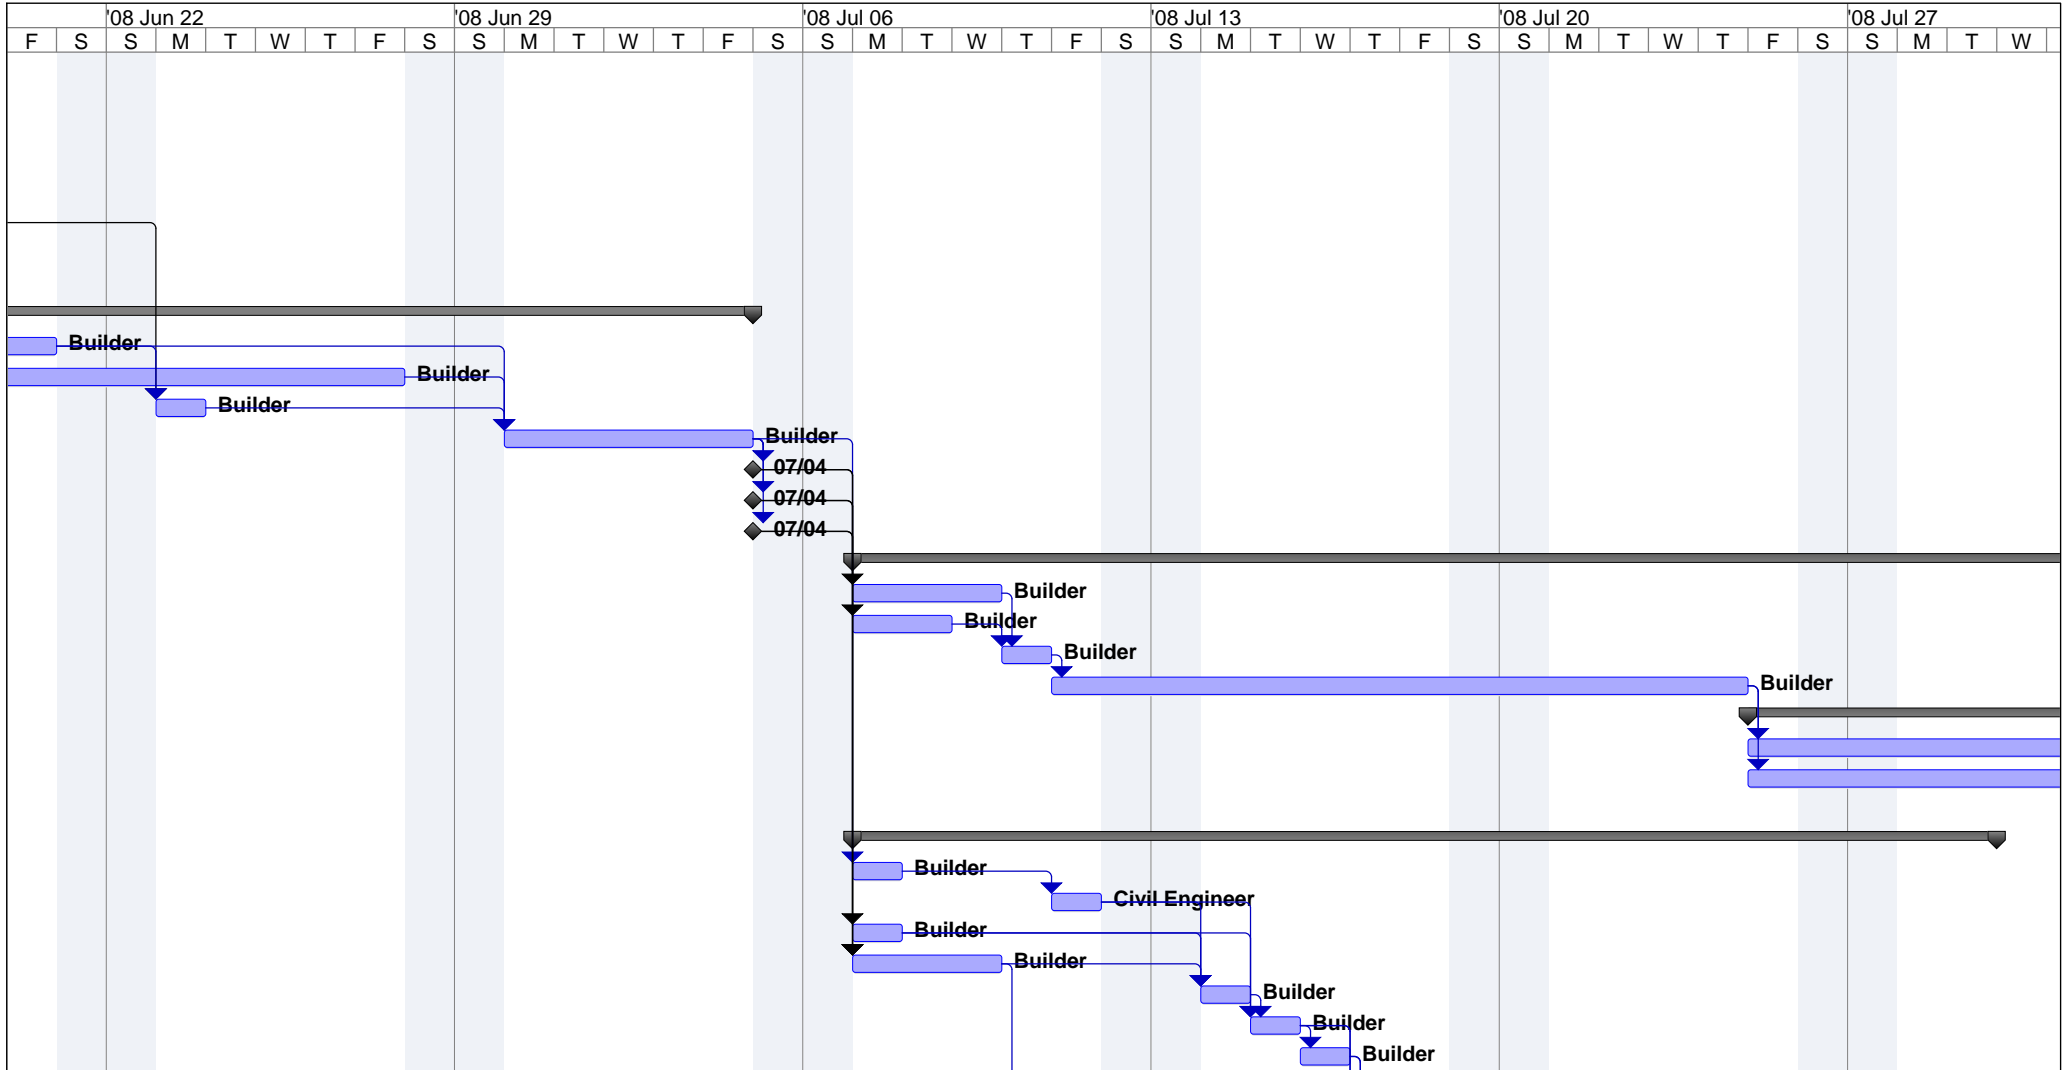


Project: b4ubuild_sample_07a
 Date: Tue 16/07/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	


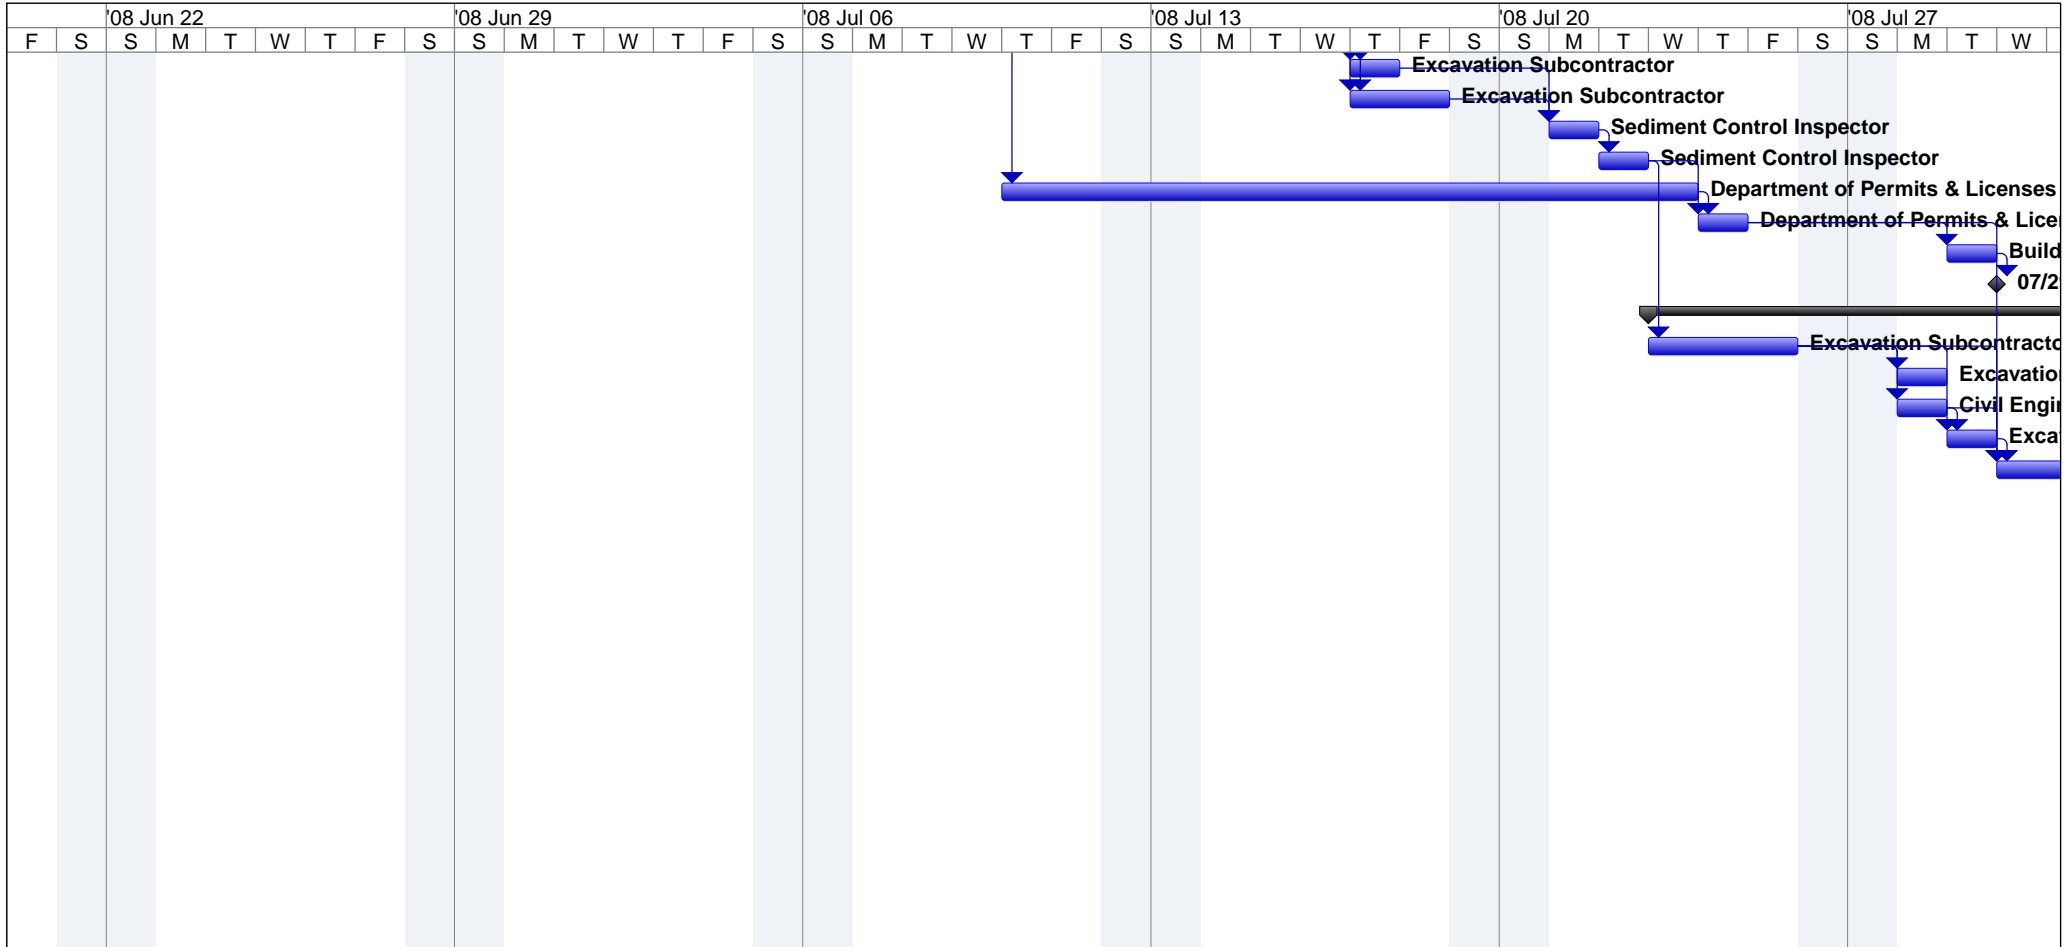


Project: b4ubuild_sample_07a Date: Tue 16/07/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	

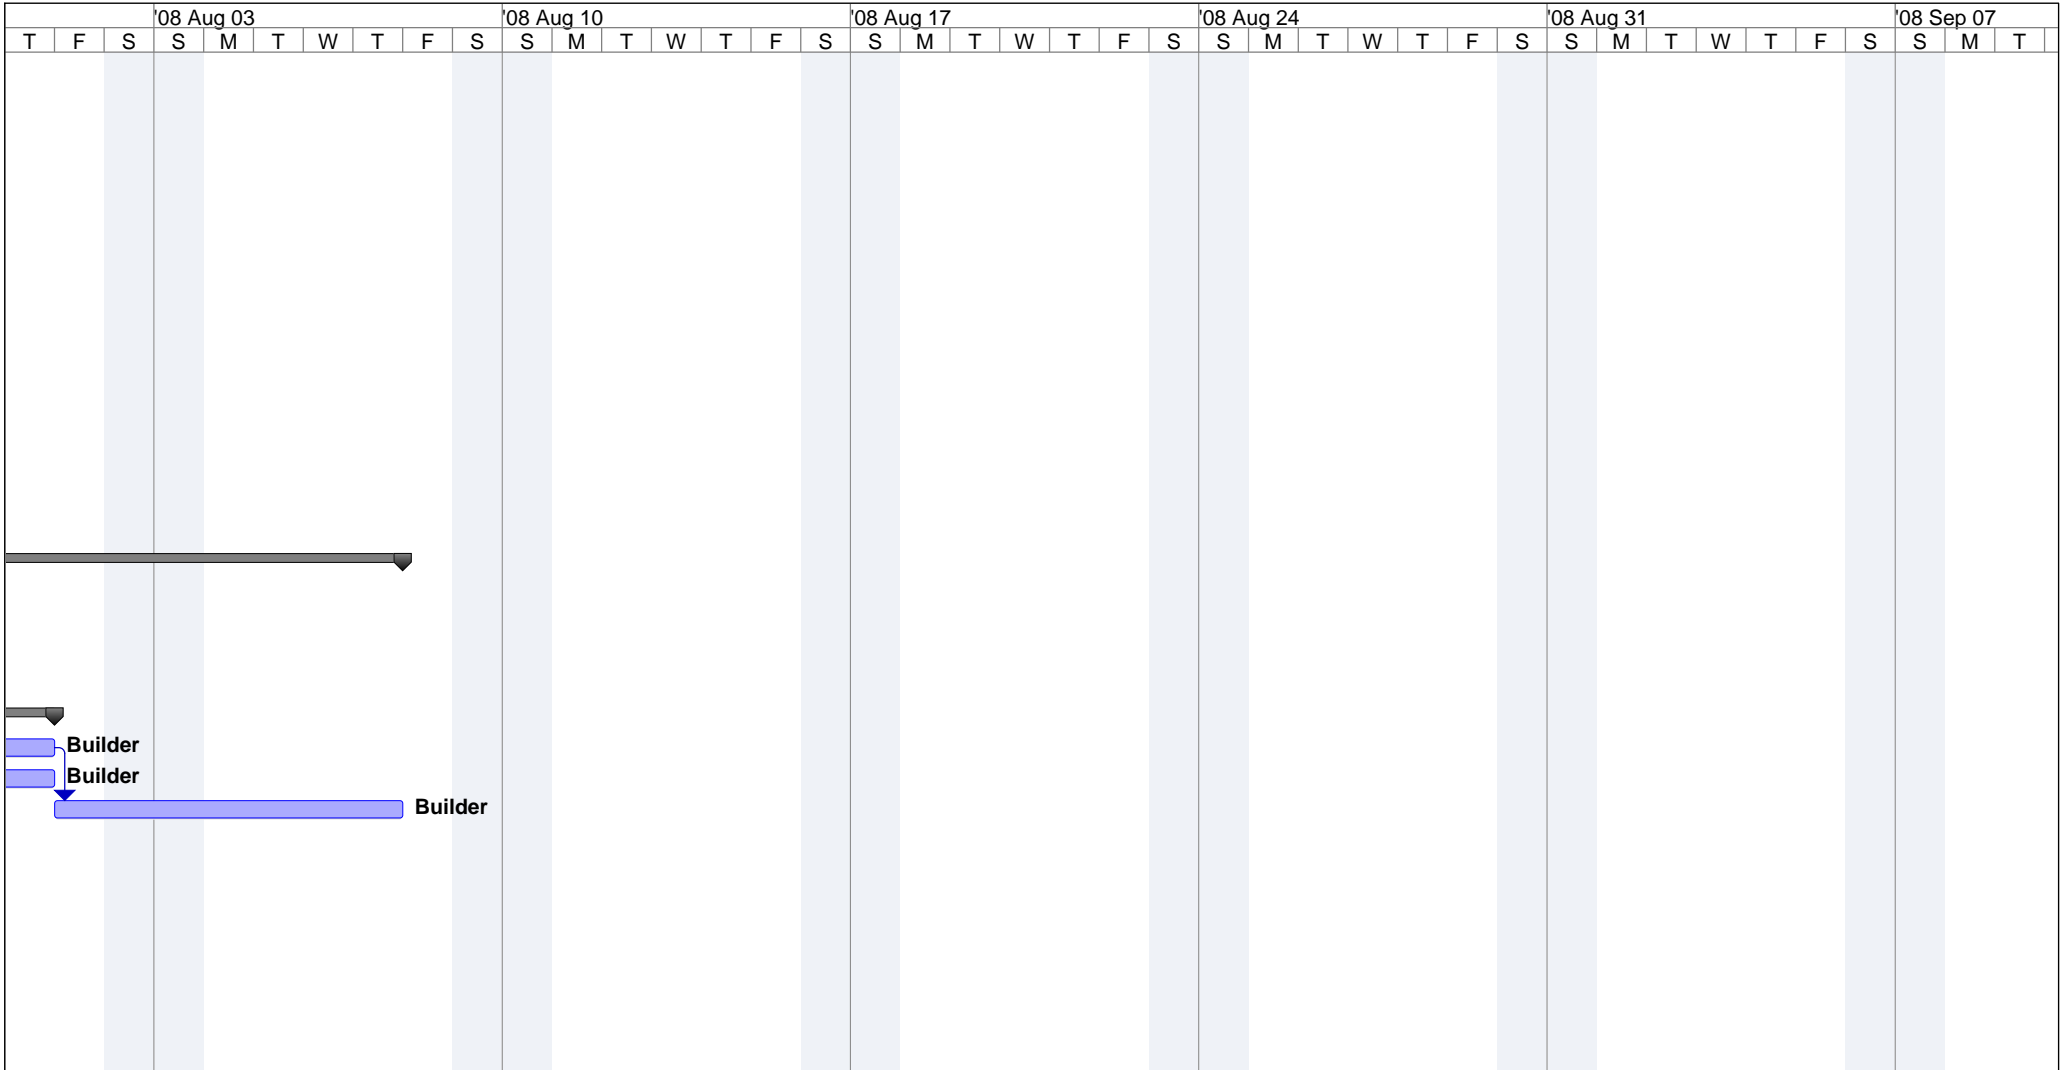

Project: b4ubuild_sample_07a
Date: Tue 16/07/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

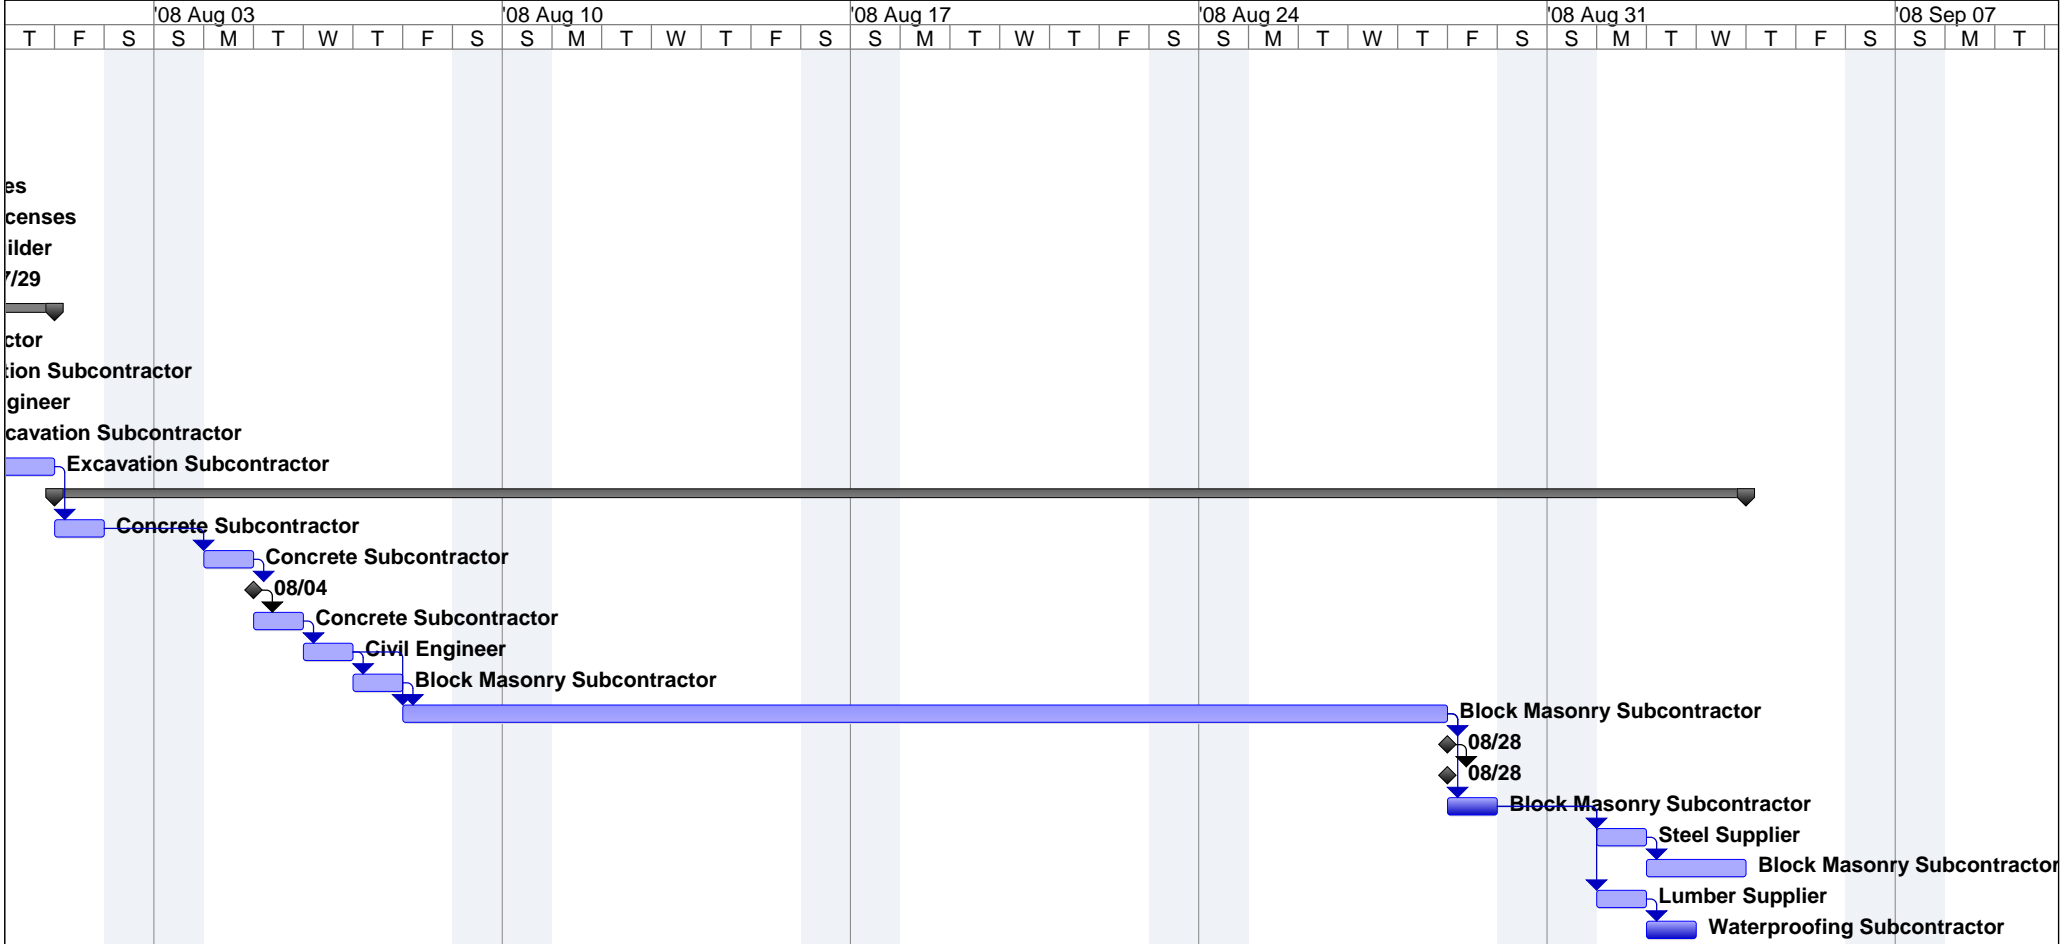

Project: b4ubuild_sample_07a Date: Tue 16/07/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	
