





ID	Task Name	Duration	Start	Finish	'08 Jun 01							'08 Jun 08							'08 Jun 15						
					S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F
34	Install Construction Entrance	1 day	Thu 08/07/17	Thu 08/07/17																					
35	Install Sediment Controls	2 days	Thu 08/07/17	Fri 08/07/18																					
36	Sediment Control Insp.	1 day	Mon 08/07/21	Mon 08/07/21																					
37	Grading Permit Issued	1 day	Tue 08/07/22	Tue 08/07/22																					
38	County Permit Process	10 days	Thu 08/07/10	Wed 08/07/23																					
39	Building Permit Approved	1 day	Thu 08/07/24	Thu 08/07/24																					
40	Pay Permit Fees and Excise Taxes	1 day	Tue 08/07/29	Tue 08/07/29																					
41	Building Permit Issued	0 days	Tue 08/07/29	Tue 08/07/29																					
42	<b>Site Work</b>	<b>7 days</b>	<b>Wed 08/07/23</b>	<b>Thu 08/07/31</b>																					
43	Clear Lot	3 days	Wed 08/07/23	Fri 08/07/25																					
44	Strip Topsoil & Stockpile	1 day	Mon 08/07/28	Mon 08/07/28																					
45	Stake Lot for Excavation	1 day	Mon 08/07/28	Mon 08/07/28																					
46	Rough grade lot	1 day	Tue 08/07/29	Tue 08/07/29																					
47	Excavate for foundation	2 days	Wed 08/07/30	Thu 08/07/31																					
48	<b>Foundation</b>	<b>24 days</b>	<b>Fri 08/08/01</b>	<b>Wed 08/09/03</b>																					
49	Layout footings	1 day	Fri 08/08/01	Fri 08/08/01																					
50	Dig Footings & Install Reinforcing	1 day	Mon 08/08/04	Mon 08/08/04																					
51	Footing Inspection	0 days	Mon 08/08/04	Mon 08/08/04																					
52	Pour footings	1 day	Tue 08/08/05	Tue 08/08/05																					
53	Pin Footings	1 day	Wed 08/08/06	Wed 08/08/06																					
54	Stock Block, Mortar, Sand	1 day	Thu 08/08/07	Thu 08/08/07																					
55	Build Block Foundation	15 days	Fri 08/08/08	Thu 08/08/28																					
56	Foundation Certification	0 days	Thu 08/08/28	Thu 08/08/28																					
57	Draw #1 (Location Survey)	0 days	Thu 08/08/28	Thu 08/08/28																					
58	Fill Block Cores w/ Concrete	1 day	Fri 08/08/29	Fri 08/08/29																					
59	Steel Delivery	1 day	Mon 08/09/01	Mon 08/09/01																					
60	Set Lintels, Bolts, Cap Block	2 days	Tue 08/09/02	Wed 08/09/03																					
61	Lumber Delivery	1 day	Mon 08/09/01	Mon 08/09/01																					
62	Waterproofing and Drain Tile	1 day	Tue 08/09/02	Tue 08/09/02																					

Project: b4ubuild\_sample\_07a  
Date: Tue 16/07/12


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

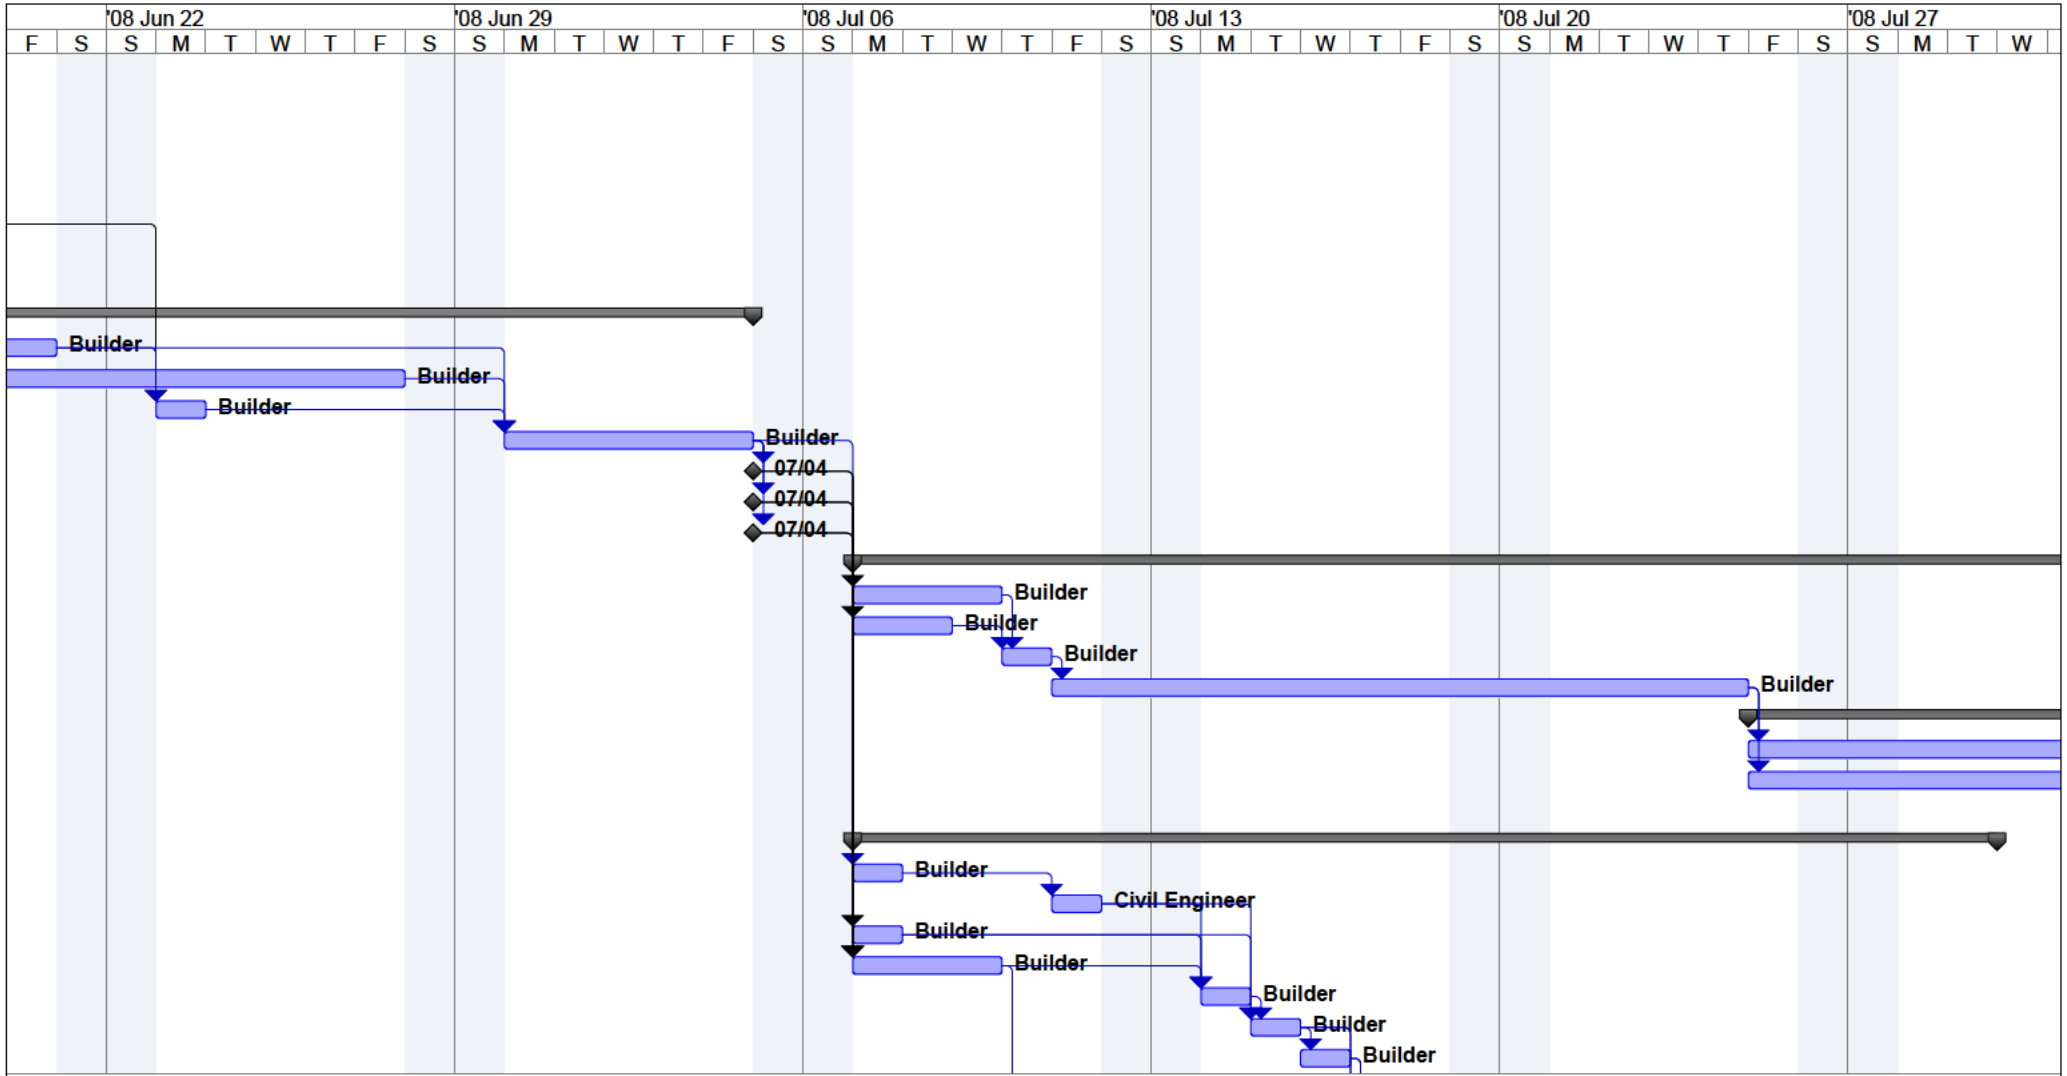


Project: b4ubuild_sample_07a Date: Tue 16/07/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	

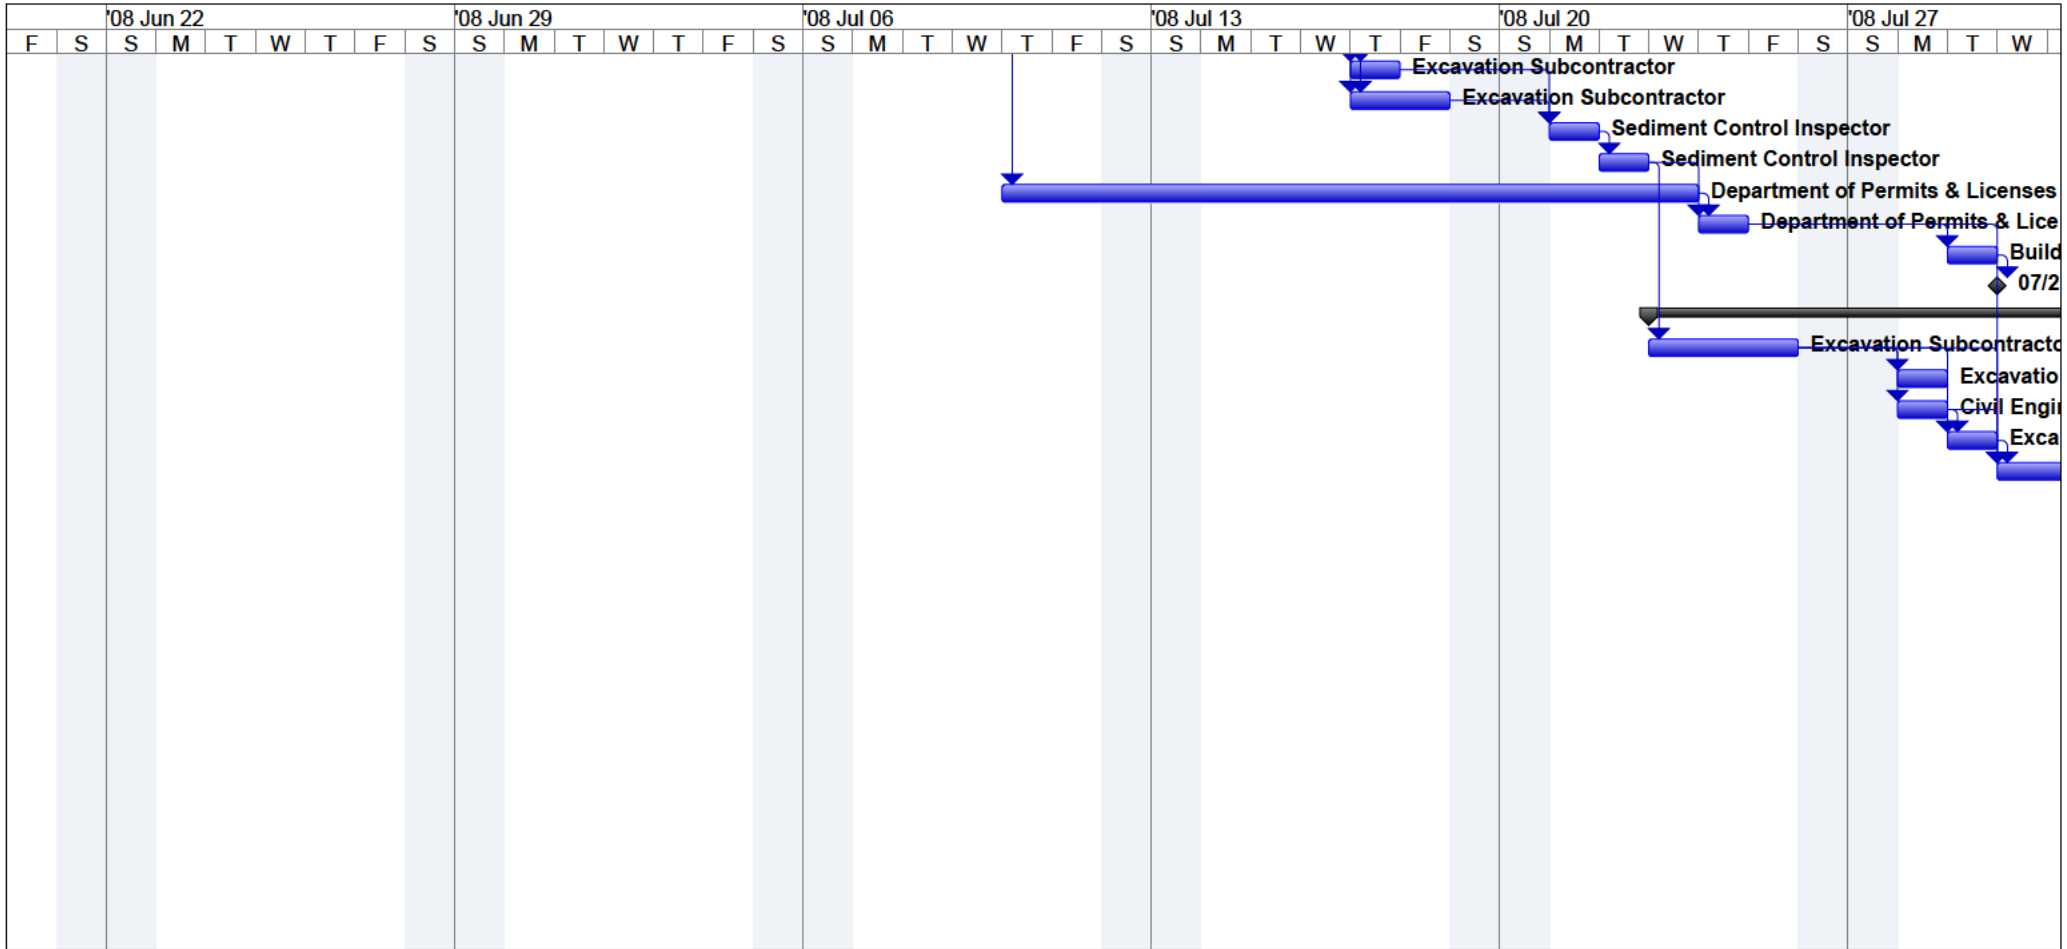

Project: b4ubuild_sample_07a Date: Tue 16/07/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	

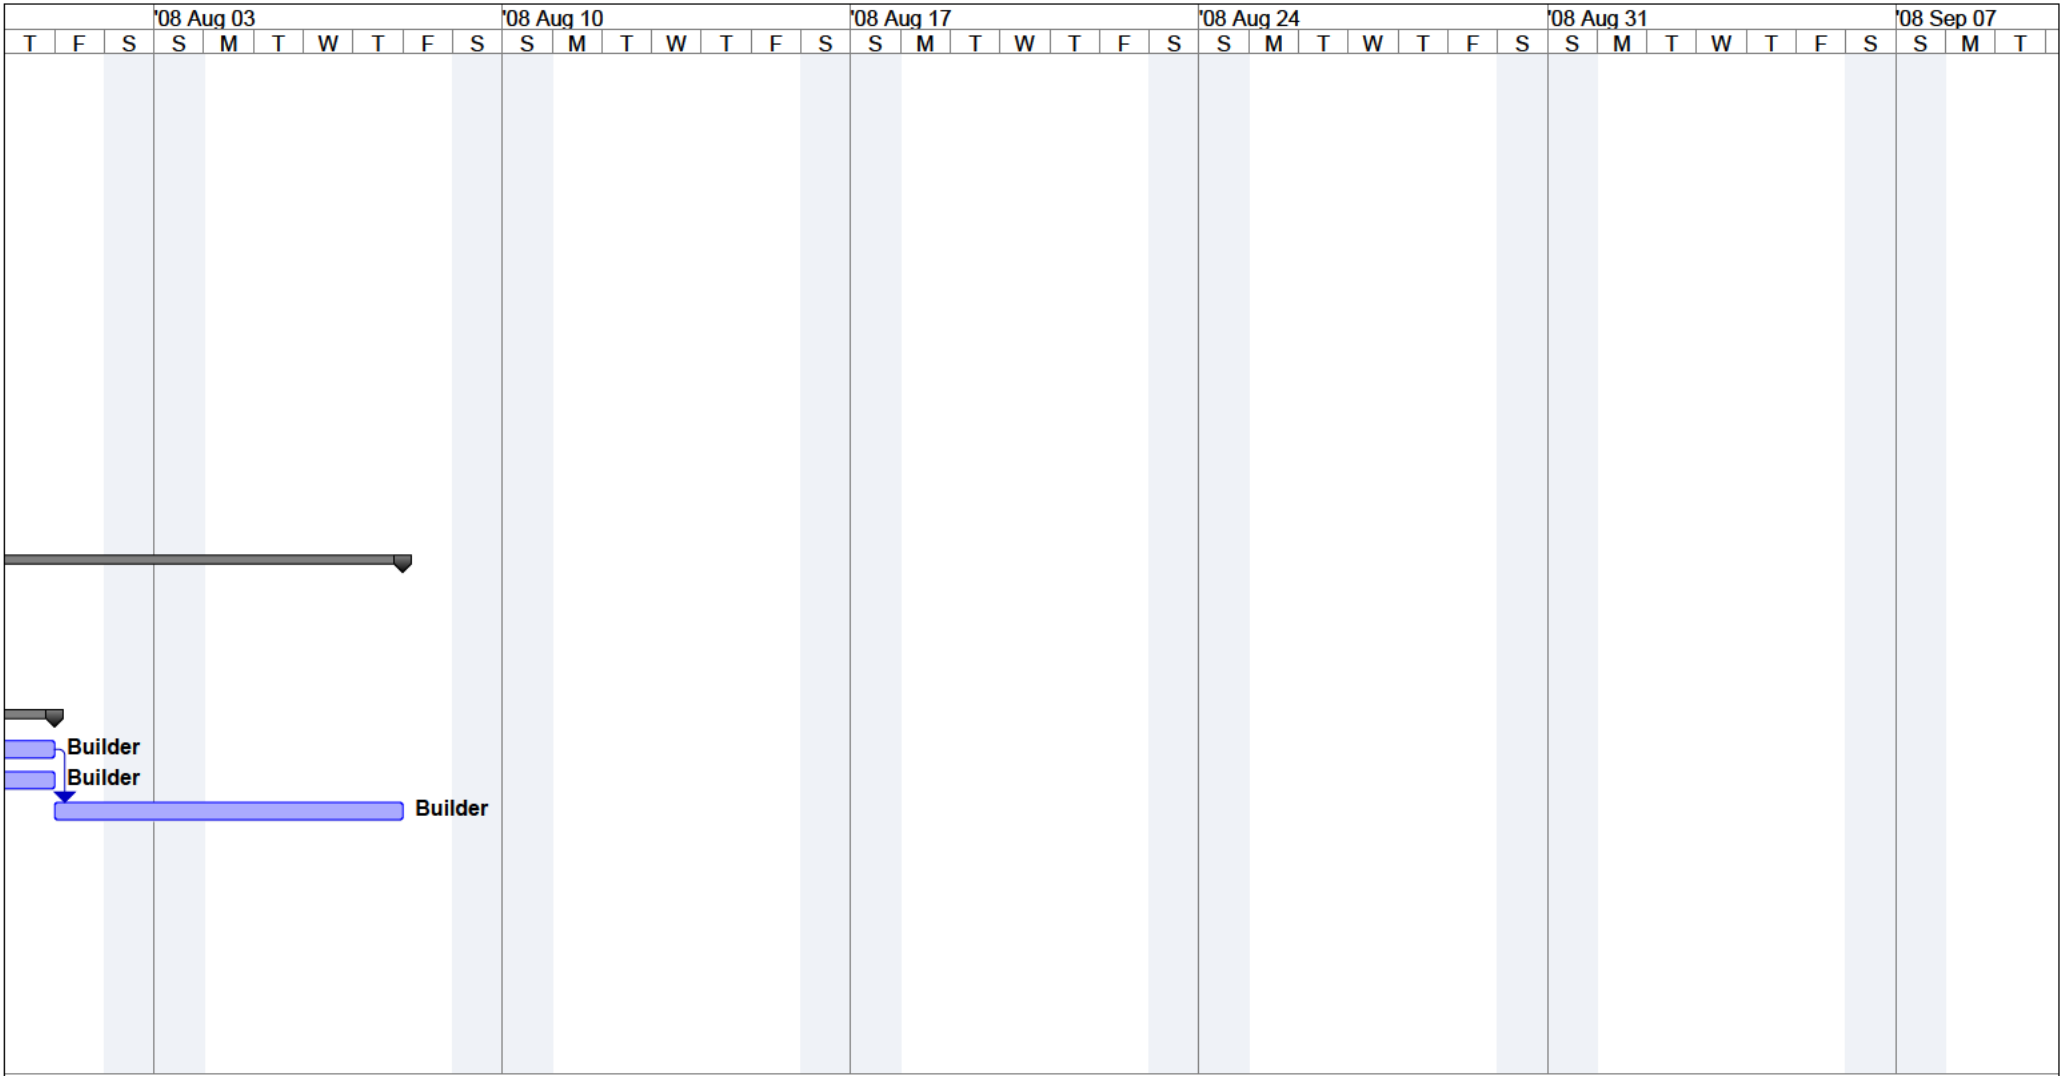

Project: b4ubuild_sample_07a Date: Tue 16/07/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	

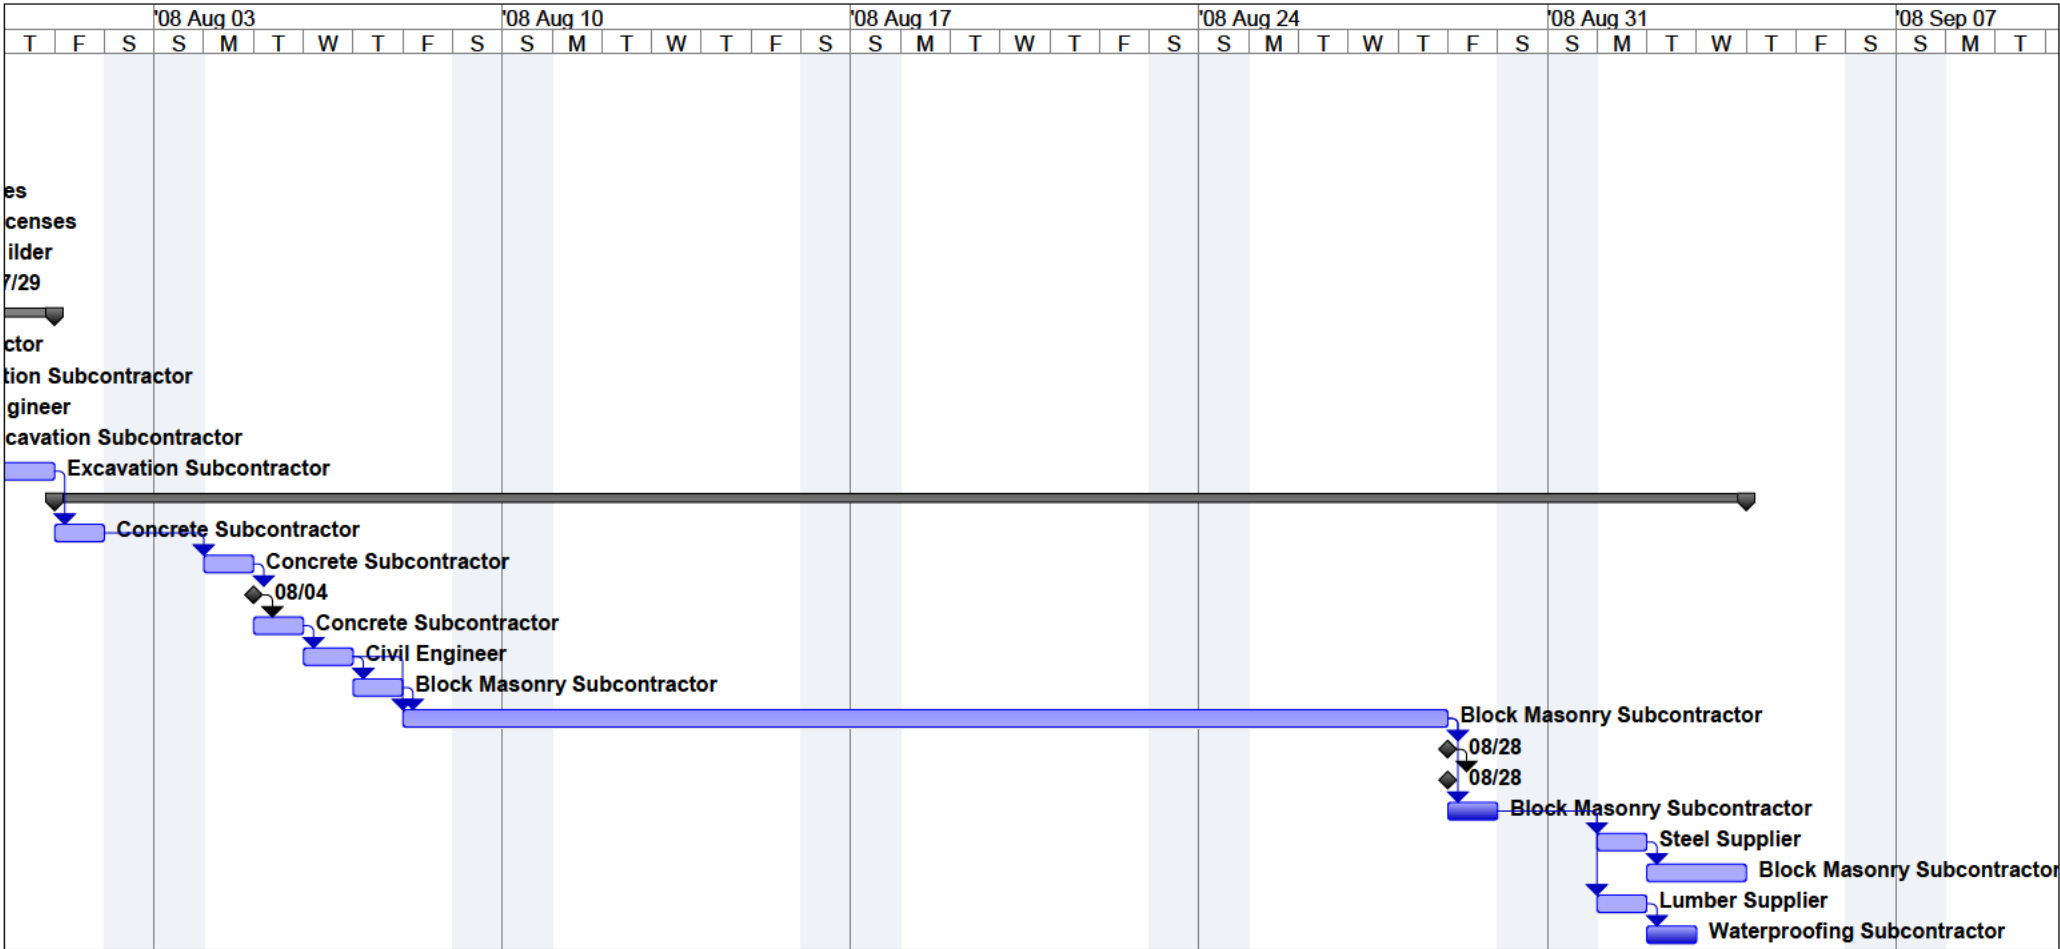

es  
censes  
ilder  
7/29  
ctor  
tion Subcontractor  
gineer  
cavation Subcontractor  
Excavation Subcontractor  
Concrete Subcontractor  
Concrete Subcontractor  
08/04  
Concrete Subcontractor  
Civil Engineer  
Block Masonry Subcontractor  
Block Masonry Subcontractor  
08/28  
08/28  
Block Masonry Subcontractor  
Steel Supplier  
Block Masonry Subcontractor  
Lumber Supplier  
Waterproofing Subcontractor

Project: b4ubuild_sample_07a Date: Tue 16/07/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	
